
## JUNE 2005 FILING DATE

## **TOKENEKE ELEMENTARY SCHOOL**

Schedules for Options "A", "A-1" & "C" Based on June 2005 Filing Date with the State Dept. of Education

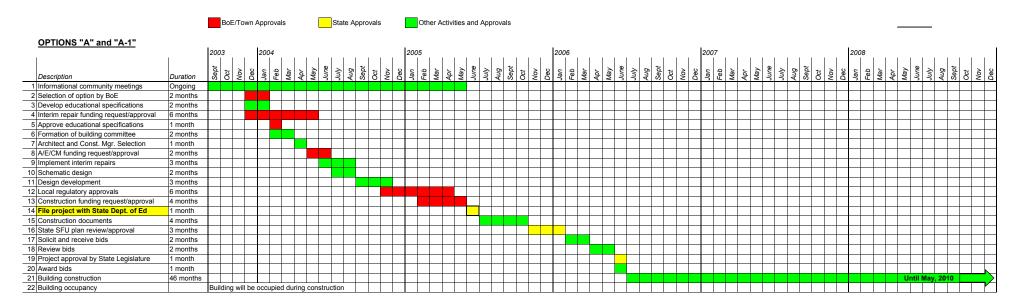

OPTION "C"		2003	,	20	004								2005	:							Ì	2006								2	007								200	เกล							
Description	Duration	Sept 2	\ok	oec V	ge qu	/ar	lpr Aay	lune	luly	Sept	Jor Vov	Dec	lan g	q <sub>e-</sub>	Apr	Aay	une	Aug	Sept	Vov	Sec	lan 49	-ep	Apr	/ay	luly	lug Sont	oept Oct	Vov	Sec	an eb	/ar	lpr Ani	lune	luly	Aug	oept Oct	Vov	Jec lan	ge	/ar	Apr Aav	lune	/m/	lug Sept	Oct	
Informational community meetings	Ongoing	0,	<u> </u>	7	, 4		1 -	3	3 1	0) (	J 2	7	3				, ,	_	0) (		7	, 4	_	_		, ,		, 0	_	7	, «		1 -	,	,	`	,, 0		4	-	_	1 -		-) -)	. 0,		Ť
Selection of option by BoE	2 months																														1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	+
Develop educational specifications	2 months																																					Ħ	$\top$	$\Box$			$\top$			1	Ť
Interim repair funding request/approval	6 months																																							$\Box$							T
Approve educational specifications	1 month					П					1																				1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	T
Formation of building committee	2 months	H									1	$\top$		T														1	Ħ	1	1							$\Box$	+	$\vdash$	†		+	_	+	1	t
Architect and Const. Mgr. Selection	1 month										1																	1			1							H	$\top$	$\Box$			$\top$		$\top$	1	T
A/E/CM funding request and approval	2 months										1																				1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	Ť
Implement interim repairs	3 months										1																				1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	Ť
Schematic design	2 months																																					$\vdash$	+	+	$\vdash$		+	$\neg$	+	+	†
Design development	3 months																														1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	Ť
Local regulatory approvals	6 months																																					Ħ	$\top$	$\Box$			$\top$			1	Ť
Construction funding request/approval	4 months																																							$\Box$							Ť
File project with State Dept. of Ed.	1 month																																							$\Box$							T
Construction documents	6 months										1																				1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	Ť
State SFU plan review/approval	3 months										1																				1							Ħ	$\top$	$\Box$	T			$\neg$	+	1	Ť
Solicit and receive bids	2 months				1						1	1																1	H		1							H	1	$\vdash$			+		+	1	Ť
Review bids	2 months				1						1																	1			1							H	$\top$	$\Box$			$\top$		$\top$	1	T
Project approval by State Legislature	1 month																																					Ħ	1	$\Box$	T		$\top$			1	Ť
Award bids	1 month				1	H					1	$\Box$									$\Box$							1	Ħ		1	T			$\Box$			Ħ	1	$\vdash$	$\neg$		+		+	1	Ť
Building construction	16 months										1																												$\top$	+			+	$\neg$	+	1	t
Relocation process	1 month	H			1						1	T		T																										$\vdash$	†		+	_	+	1	Ť
Building occupancy		H			1						1	T		T														1	Ħ	1	1										†		+	_	+	1	T
Completion of site work/demo	8 months						-				_			-		_	_	1 +	_	_			1				_		1 1		_			_			1		_							+	+
