Wetland/Wetland Buffer Restoration Plan

For 4 Four Acres Road in Darien, CT

By Aleksandra Moch, Wetland Scientist and Landscape Designer, April 27, 2021

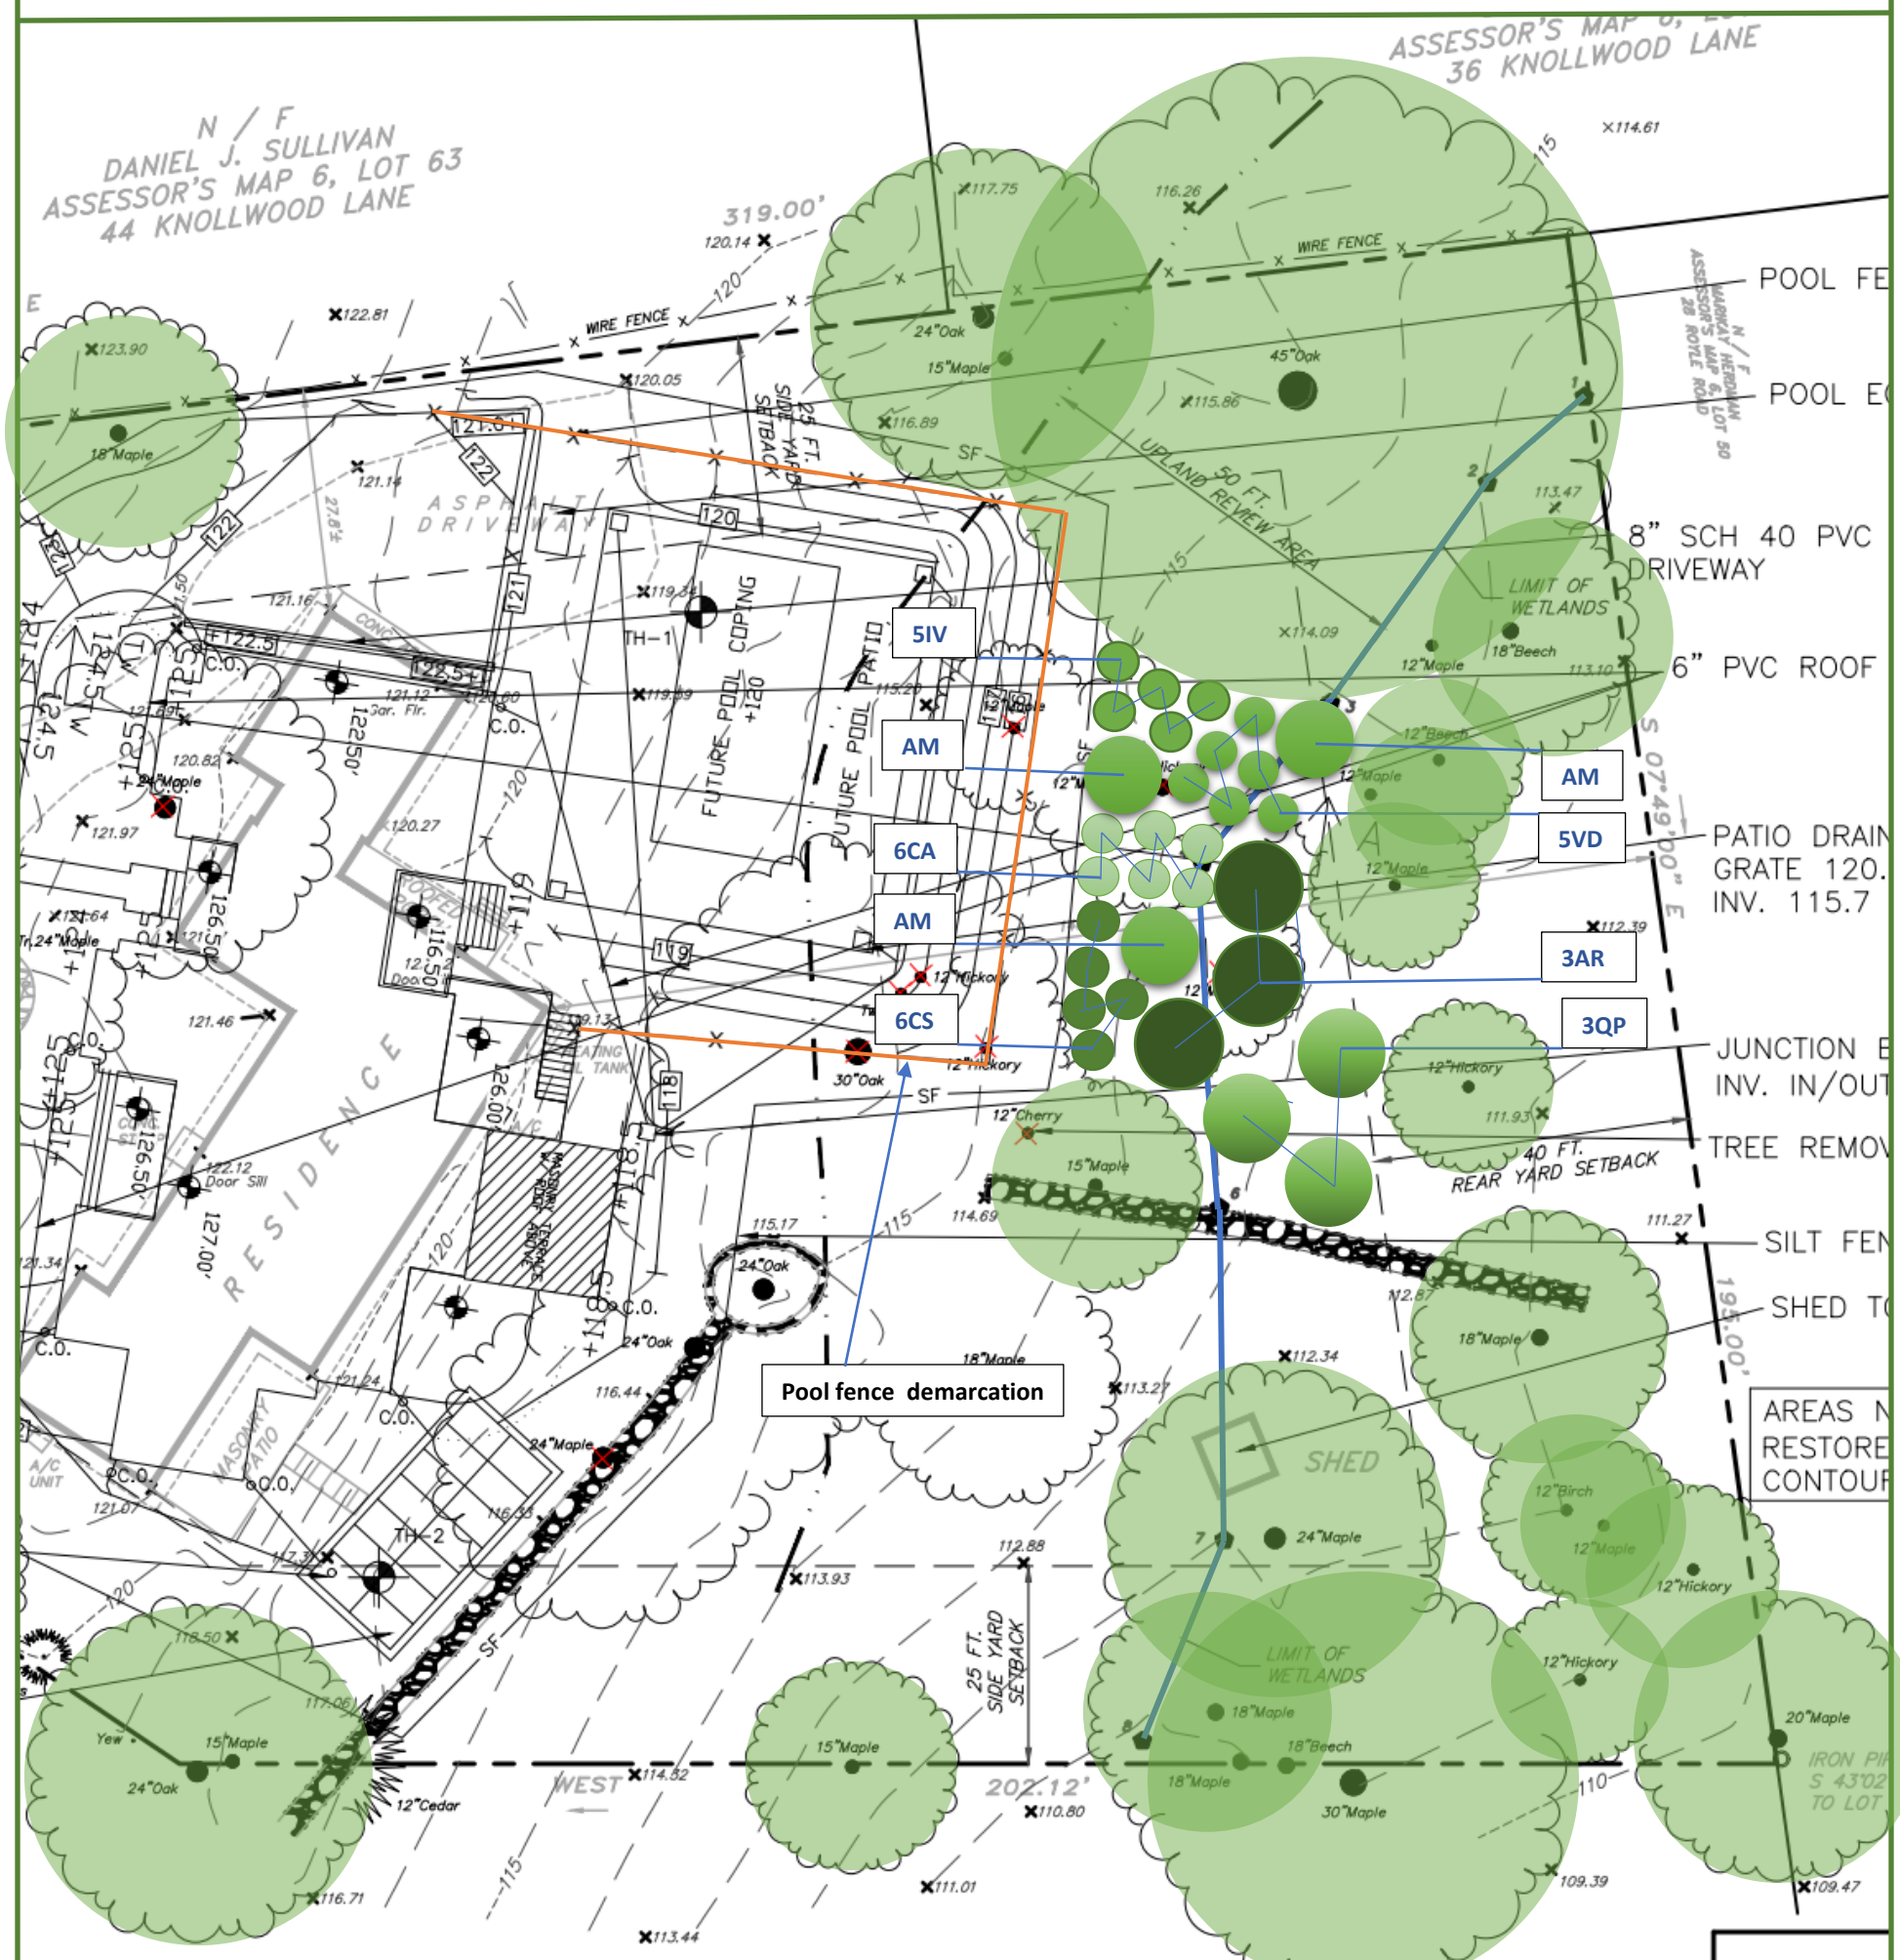

Planting Schedule

QTY	KEY	BOTANICAL/COMMON NAME	SIZE	ROOT
Trees:				
3	AR	Acer rubrum / Red maple	6'-7'	B&B
3	QP	Quercus palustris / Pin oak	6'-7'	B&B
3	AM	Amelanchier arborea / Serviceberry	5'-6'	B&B
Shrubs:				
6	CS	Cornus servicea / Red osier dogwood	3'-4'	Cont.
6	CA	Clethra alifolia / Summersweet	2'-3'	Cont.
5	VD	Viburnum dentatum / Arrowwood viburnum	3'-4'	Cont.
5	IV	Ilex verticillate / Winterberry	2'-3'	Cont.
